



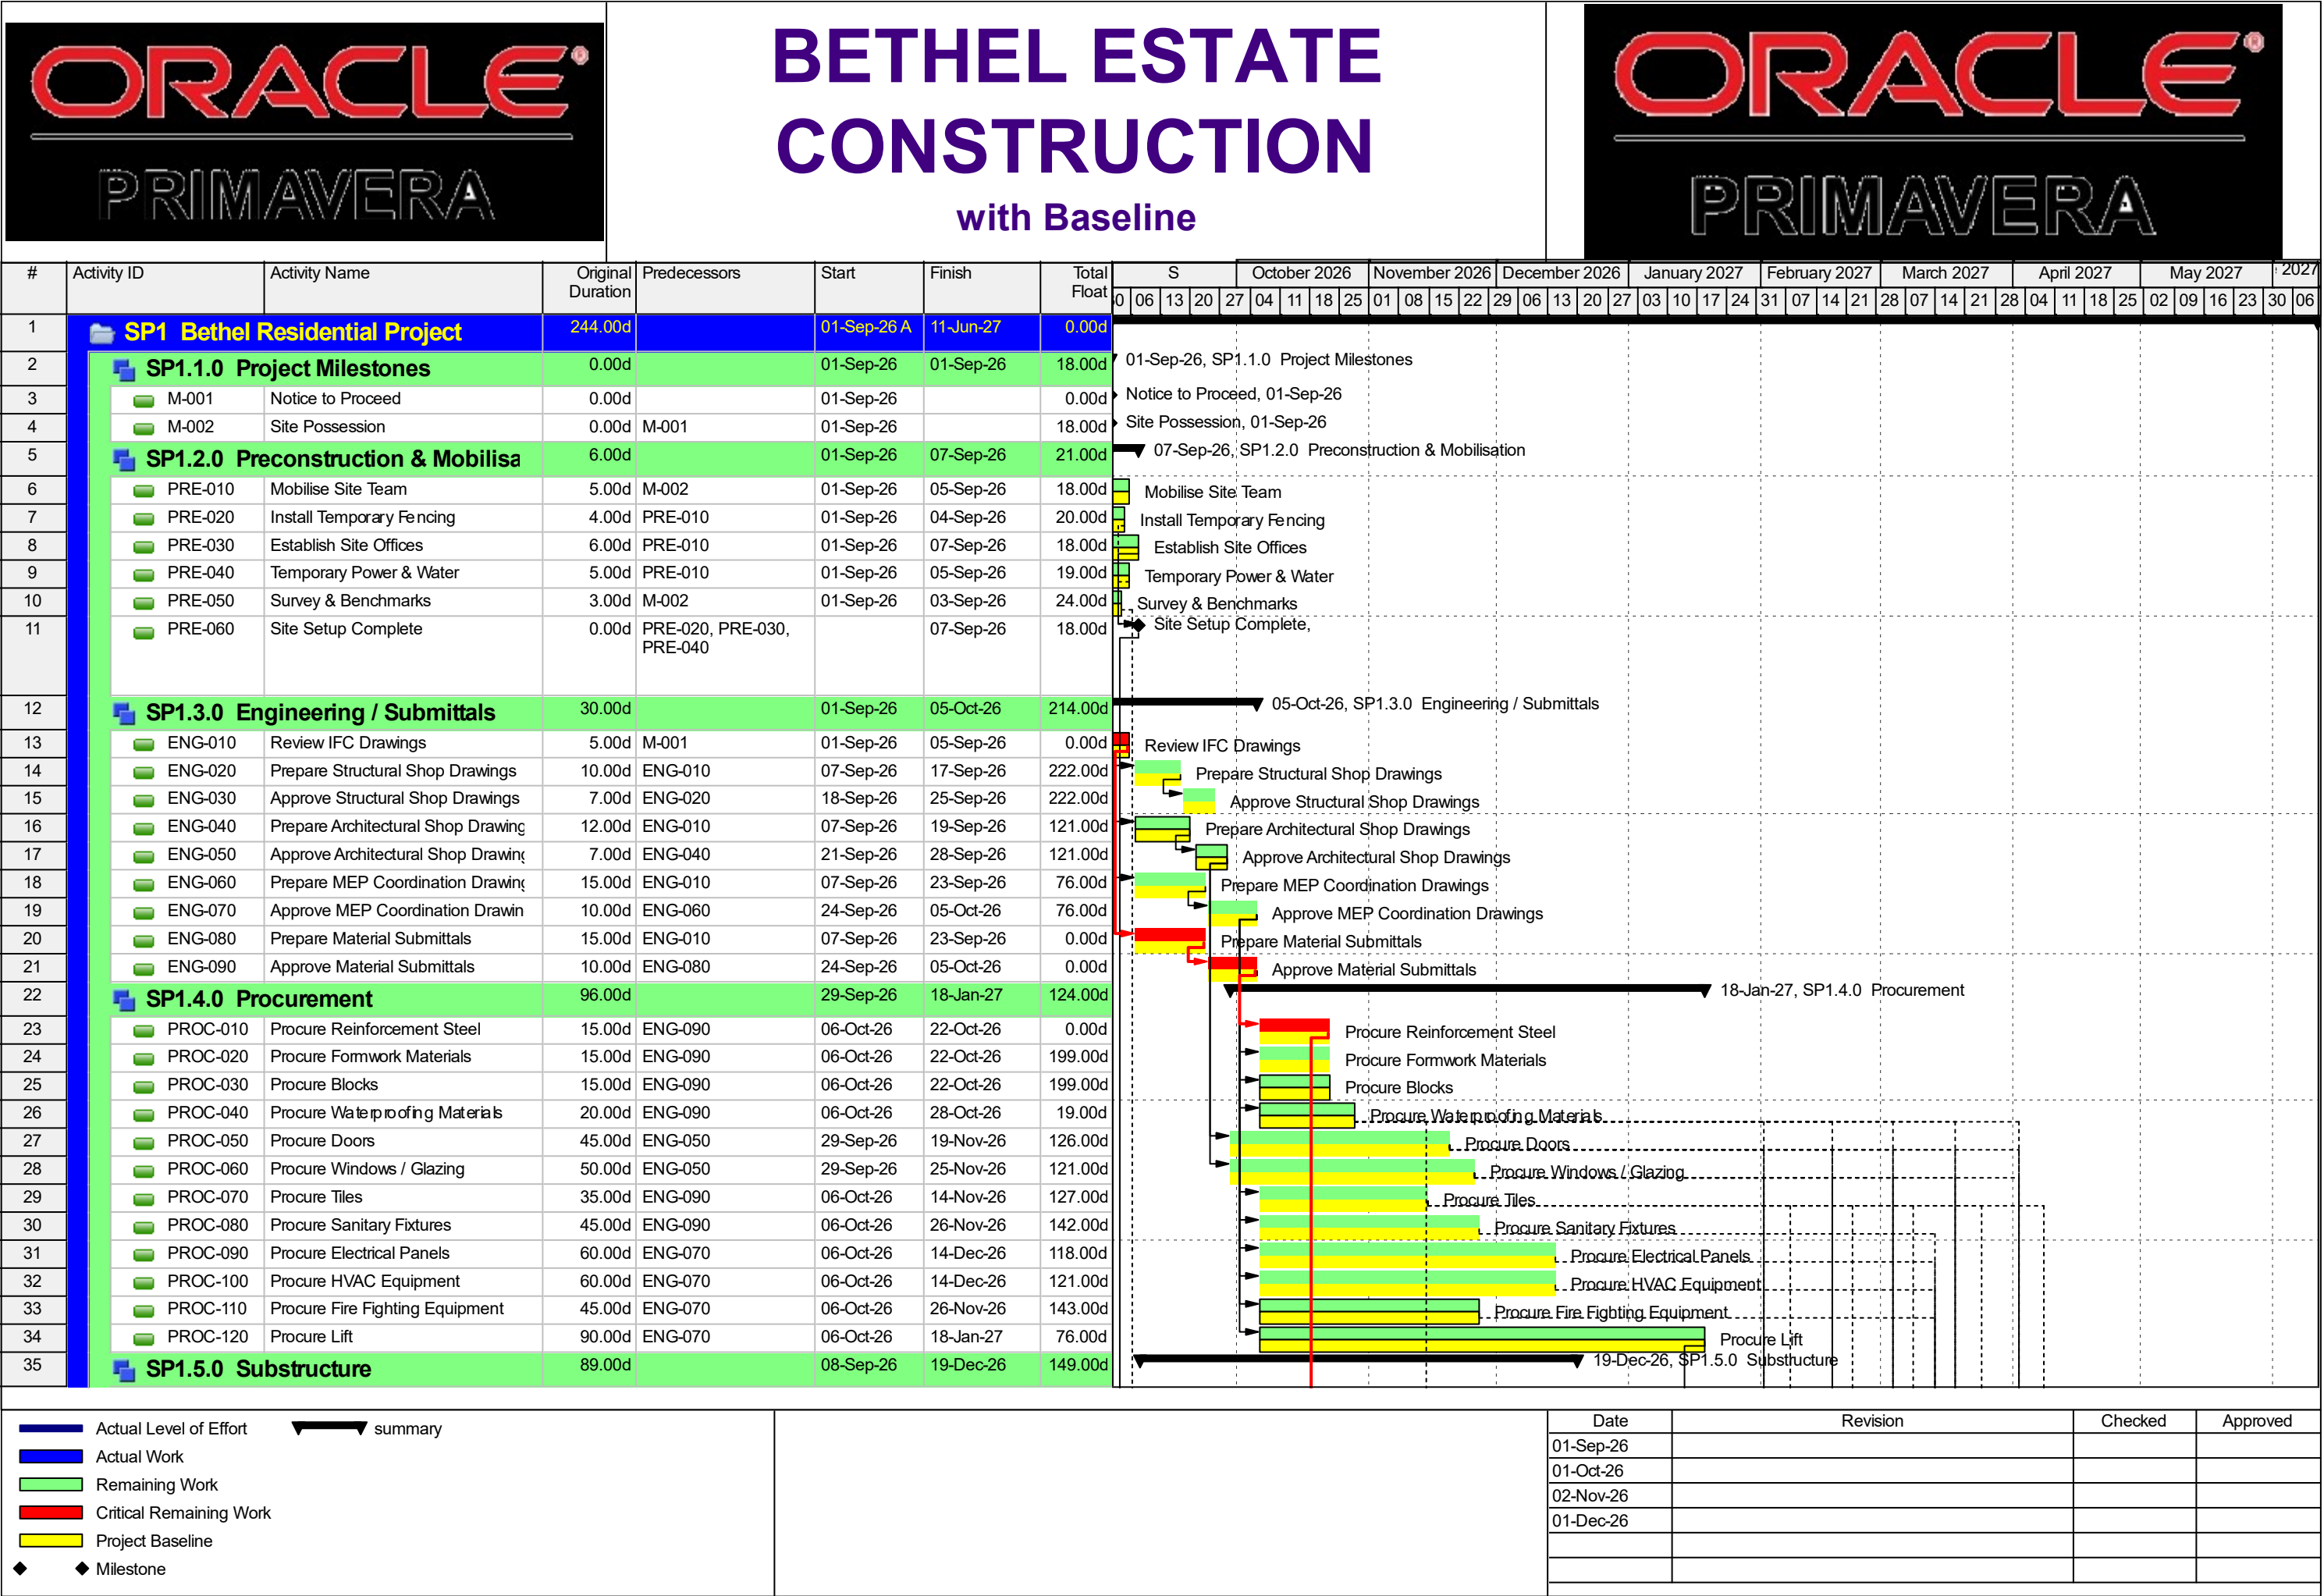

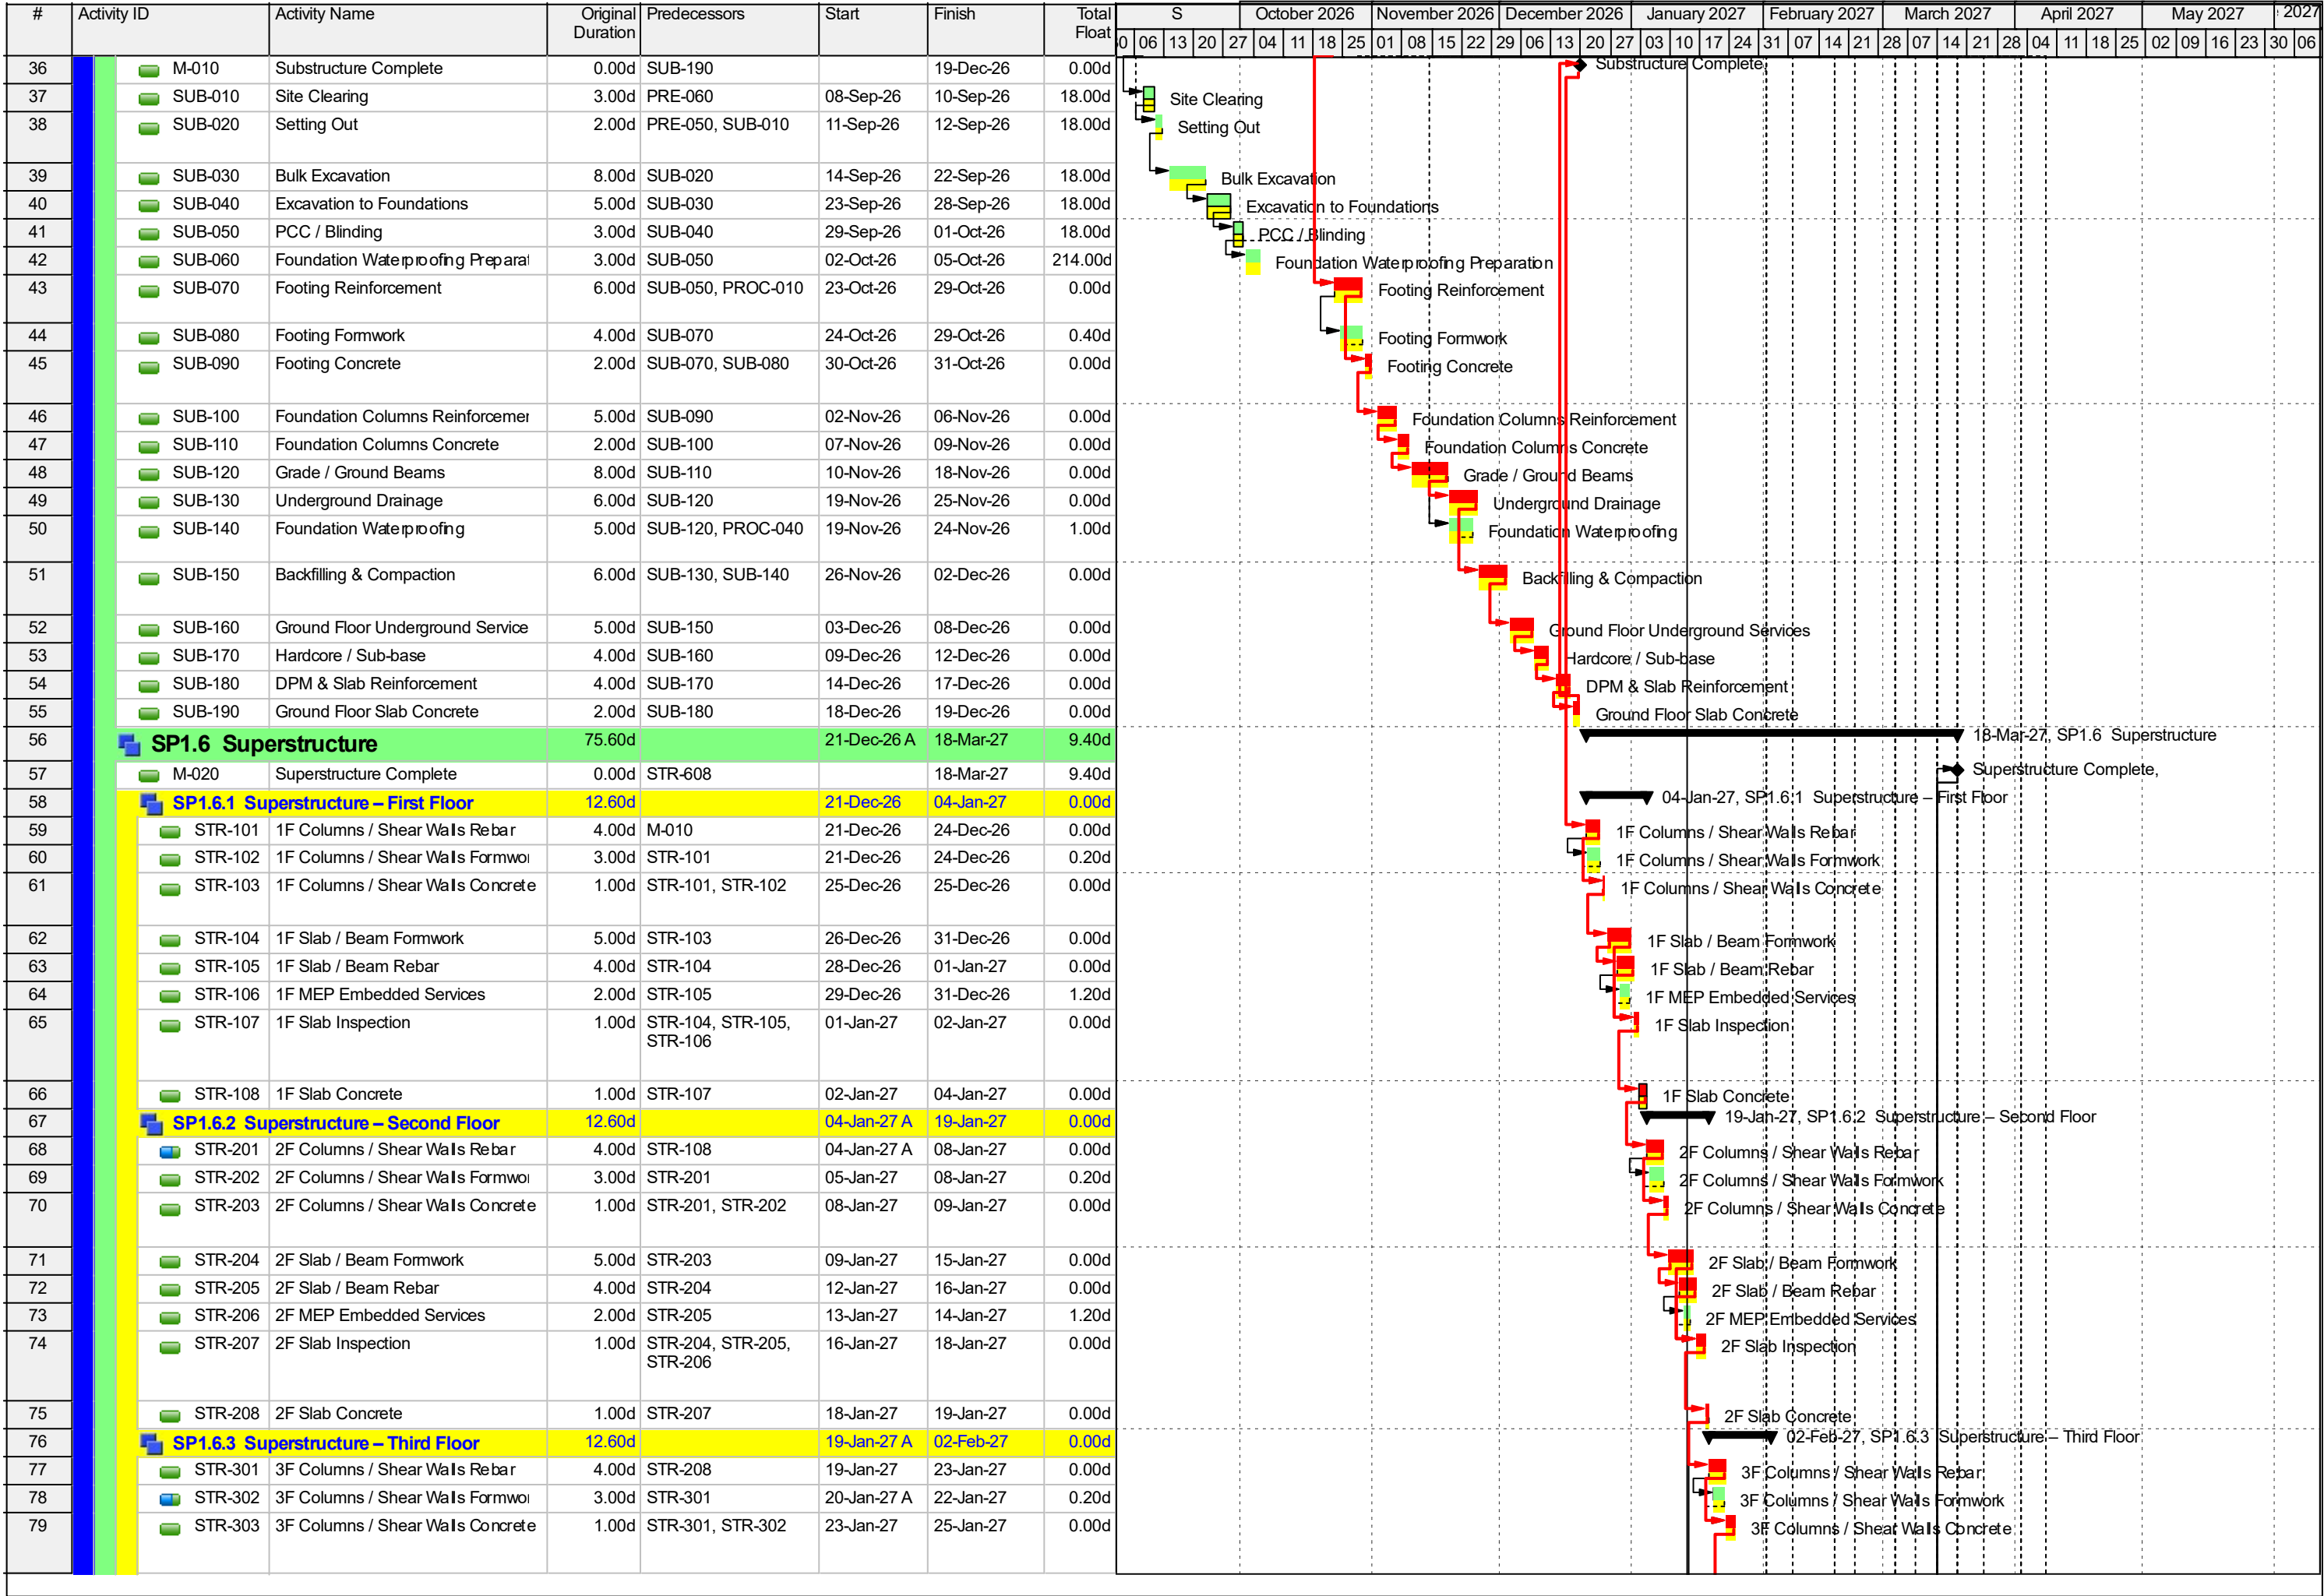

#	Activity ID	Activity Name	Original Duration	Predecessors	Start	Finish	Total Float	2027																																																
								S	October 2026					November 2026				December 2026				January 2027				February 2027				March 2027				April 2027				May 2027																		
								0	06	13	20	27		04	11	18	25		01	08	15	22		29	06	13	20	27		03	10	17	24		31	07	14	21		28	07	14	21		28	04	11	18	25		02	09	16	23	30	06
121		ARC-108	1F Doors & Windows	5.00d	ARC-103, PROC-050, PROC-060	06-Feb-27	12-Feb-27	87.40d																																																
122		ARC-109	1F False Ceiling	5.00d	ARC-106	12-Feb-27	18-Feb-27	81.40d																																																
123		ARC-110	1F First Coat Painting	5.00d	ARC-103	06-Feb-27	12-Feb-27	86.40d																																																
124		ARC-111	1F MEP Second Fix	6.00d	ARC-107, ARC-109, ARC-110	20-Feb-27	27-Feb-27	79.40d																																																
125		ARC-112	1F Joinery & Fixtures	5.00d	ARC-107, ARC-108	20-Feb-27	26-Feb-27	80.40d																																																
126		ARC-113	1F Final Painting	4.00d	ARC-111, ARC-112	27-Feb-27	04-Mar-27	79.40d																																																
127		ARC-114	1F Final Floor Finishes	4.00d	ARC-113	04-Mar-27	09-Mar-27	79.40d																																																
128		ARC-115	1F Final Cleaning	2.00d	ARC-114	09-Mar-27	11-Mar-27	79.40d																																																
129		SP1.7.2 Architectural – Second Floor		44.40d		02-Feb-27 A	26-Mar-27	66.80d																																																
130		ARC-201	2F Blockwork	8.00d	STR-308	02-Feb-27	11-Feb-27	66.80d																																																
131		ARC-202	2F MEP First Fix	7.00d	ARC-201	05-Feb-27	13-Feb-27	66.80d																																																
132		ARC-203	2F Internal Plaster	7.00d	ARC-201, ARC-202	13-Feb-27	22-Feb-27	66.80d																																																
133		ARC-204	2F Wet Area Waterproofing	4.00d	ARC-203, PROC-040	22-Feb-27	26-Feb-27	67.80d																																																
134		ARC-205	2F Floor Screed	5.00d	ARC-203	22-Feb-27 A	27-Feb-27	66.80d																																																
135		ARC-206	2F Ceiling Framing	5.00d	ARC-203	22-Feb-27	27-Feb-27	68.80d																																																
136		ARC-207	2F Wall / Floor Tiling	7.00d	ARC-204, ARC-205, PROC-070	27-Feb-27	08-Mar-27	66.80d																																																
137		ARC-208	2F Doors & Windows	5.00d	ARC-203, PROC-050, PROC-060	22-Feb-27	27-Feb-27	74.80d																																																
138		ARC-209	2F False Ceiling	5.00d	ARC-206	27-Feb-27	05-Mar-27	68.80d																																																
139		ARC-210	2F First Coat Painting	5.00d	ARC-203	22-Feb-27	27-Feb-27	73.80d																																																
140		ARC-211	2F MEP Second Fix	6.00d	ARC-207, ARC-209, ARC-210	08-Mar-27	15-Mar-27	66.80d																																																
141		ARC-212	2F Joinery & Fixtures	5.00d	ARC-207, ARC-208	08-Mar-27	13-Mar-27	67.80d																																																
142		ARC-213	2F Final Painting	4.00d	ARC-211, ARC-212	15-Mar-27	19-Mar-27	66.80d																																																
143		ARC-214	2F Final Floor Finishes	4.00d	ARC-213	19-Mar-27	24-Mar-27	66.80d																																																
144		ARC-215	2F Final Cleaning	2.00d	ARC-214	24-Mar-27	26-Mar-27	66.80d																																																
145		SP1.7.3 Architectural – Third Floor		44.40d		17-Feb-27 A	09-Apr-27	54.20d																																																
146	ARC-301	3F Blockwork	8.00d	STR-408	17-Feb-27	26-Feb-27	54.20d																																																	
147	ARC-302	3F MEP First Fix	7.00d	ARC-301	19-Feb-27	27-Feb-27	54.20d																																																	
148	ARC-303	3F Internal Plaster	7.00d	ARC-301, ARC-302	27-Feb-27	08-Mar-27	54.20d																																																	
149	ARC-304	3F Wet Area Waterproofing	4.00d	ARC-303, PROC-040	08-Mar-27	12-Mar-27	55.20d																																																	
150	ARC-305	3F Floor Screed	5.00d	ARC-303	08-Mar-27	13-Mar-27	54.20d																																																	
151	ARC-306	3F Ceiling Framing	5.00d	ARC-303	08-Mar-27	13-Mar-27	56.20d																																																	
152	ARC-307	3F Wall / Floor Tiling	7.00d	ARC-304, ARC-305, PROC-070	13-Mar-27	22-Mar-27	54.20d																																																	
153	ARC-308	3F Doors & Windows	5.00d	ARC-303, PROC-050, PROC-060	08-Mar-27	13-Mar-27	62.20d																																																	
154	ARC-309	3F False Ceiling	5.00d	ARC-306	13-Mar-27	19-Mar-27	56.20d																																																	
155	ARC-310	3F First Coat Painting	5.00d	ARC-303	08-Mar-27	13-Mar-27	61.20d																																																	

#	Activity ID	Activity Name	Original Duration	Predecessors	Start	Finish	Total Float	September 2026							October 2026					November 2026					December 2026					January 2027					February 2027					March 2027					April 2027					May 2027					2027
								0	06	13	20	27	04	11	18	25	01	08	15	22	29	06	13	20	27	03	10	17	24	31	07	14	21	28	05	12	19	26	02	09	16	23	30	06											
156		ARC-311	3F MEP Second Fix	6.00d	ARC-307, ARC-309, ARC-310	22-Mar-27	29-Mar-27	54.20d																																															
157		ARC-312	3F Joinery & Fixtures	5.00d	ARC-307, ARC-308	22-Mar-27	27-Mar-27	55.20d																																															
158		ARC-313	3F Final Painting	4.00d	ARC-311, ARC-312	29-Mar-27 A	02-Apr-27	54.20d																																															
159		ARC-314	3F Final Floor Finishes	4.00d	ARC-313	02-Apr-27	07-Apr-27	54.20d																																															
160		ARC-315	3F Final Cleaning	2.00d	ARC-314	07-Apr-27	09-Apr-27	54.20d																																															
161		SP1.7.4 Architectural – Fourth Floor		44.40d		04-Mar-27	24-Apr-27	41.60d																																															
162		ARC-401	4F Blockwork	8.00d	STR-508	04-Mar-27	12-Mar-27	41.60d																																															
163		ARC-402	4F MEP First Fix	7.00d	ARC-401	06-Mar-27	15-Mar-27	41.60d																																															
164		ARC-403	4F Internal Plaster	7.00d	ARC-401, ARC-402	15-Mar-27	23-Mar-27	41.60d																																															
165		ARC-404	4F Wet Area Waterproofing	4.00d	ARC-403, PROC-040	23-Mar-27	27-Mar-27	42.60d																																															
166		ARC-405	4F Floor Screed	5.00d	ARC-403	23-Mar-27	29-Mar-27	41.60d																																															
167		ARC-406	4F Ceiling Framing	5.00d	ARC-403	23-Mar-27	29-Mar-27	43.60d																																															
168		ARC-407	4F Wall / Floor Tiling	7.00d	ARC-404, ARC-405, PROC-070	29-Mar-27	06-Apr-27	41.60d																																															
169		ARC-408	4F Doors & Windows	5.00d	ARC-403, PROC-050, PROC-060	23-Mar-27	29-Mar-27	49.60d																																															
170		ARC-409	4F False Ceiling	5.00d	ARC-406	29-Mar-27	03-Apr-27	43.60d																																															
171		ARC-410	4F First Coat Painting	5.00d	ARC-403	23-Mar-27	29-Mar-27	48.60d																																															
172		ARC-411	4F MEP Second Fix	6.00d	ARC-407, ARC-409, ARC-410	06-Apr-27	13-Apr-27	41.60d																																															
173		ARC-412	4F Joinery & Fixtures	5.00d	ARC-407, ARC-408	06-Apr-27	12-Apr-27	42.60d																																															
174		ARC-413	4F Final Painting	4.00d	ARC-411, ARC-412	13-Apr-27	17-Apr-27	41.60d																																															
175		ARC-414	4F Final Floor Finishes	4.00d	ARC-413	17-Apr-27	22-Apr-27	41.60d																																															
176		ARC-415	4F Final Cleaning	2.00d	ARC-414	22-Apr-27	24-Apr-27	41.60d																																															
177		SP1.7.5 Architectural – Fifth Floor		44.40d		18-Mar-27 A	08-May-27	0.00d																																															
178		ARC-501	5F Blockwork	8.00d	STR-608	18-Mar-27	27-Mar-27	0.00d																																															
179		ARC-502	5F MEP First Fix	7.00d	ARC-501	22-Mar-27	29-Mar-27	0.00d																																															
180		ARC-503	5F Internal Plaster	7.00d	ARC-501, ARC-502	30-Mar-27	06-Apr-27	0.00d																																															
181		ARC-504	5F Wet Area Waterproofing	4.00d	ARC-503, PROC-040	07-Apr-27	10-Apr-27	1.00d																																															
182		ARC-505	5F Floor Screed	5.00d	ARC-503	07-Apr-27	12-Apr-27	0.00d																																															
183		ARC-506	5F Ceiling Framing	5.00d	ARC-503	07-Apr-27 A	12-Apr-27	2.00d																																															
184		ARC-507	5F Wall / Floor Tiling	7.00d	ARC-504, ARC-505, PROC-070	13-Apr-27	20-Apr-27	0.00d																																															
185		ARC-508	5F Doors & Windows	5.00d	ARC-503, PROC-050, PROC-060	07-Apr-27	12-Apr-27	8.00d																																															
186		ARC-509	5F False Ceiling	5.00d	ARC-506	13-Apr-27	17-Apr-27	2.00d																																															
187		ARC-510	5F First Coat Painting	5.00d	ARC-503	07-Apr-27	12-Apr-27	7.00d																																															
188		ARC-511	5F MEP Second Fix	6.00d	ARC-507, ARC-509, ARC-510	21-Apr-27	27-Apr-27	0.00d																																															
189		ARC-512	5F Joinery & Fixtures	5.00d	ARC-507, ARC-508	21-Apr-27	26-Apr-27	1.00d																																															
190	ARC-513	5F Final Painting	4.00d	ARC-511, ARC-512	28-Apr-27	01-May-27	0.00d																																																
191	ARC-514	5F Final Floor Finishes	4.00d	ARC-513	03-May-27	06-May-27	0.00d																																																

#	Activity ID	Activity Name	Original Duration	Predecessors	Start	Finish	Total Float	2027																																	
								S	0	06	13	20	27	04	11	18	25	01	08	15	22	29	06	13	20	27	03	10	17	24	31	07	14	21	28	07	14	21	28	04	11
192	SP1.8.0 MEP Works	 ARC-515 5F Final Cleaning	2.00d	ARC-514	07-May-27	08-May-27	0.00d																																		
193				50.80d		02-Feb-27	02-Apr-27	60.40d																																	
194		 MEP-010 Main Drainage Risers	12.00d	STR-308	02-Feb-27	16-Feb-27	78.20d																																		
195		 MEP-020 Water Supply Risers	10.00d	STR-308	02-Feb-27	13-Feb-27	79.20d																																		
196		 MEP-030 Electrical Risers	12.00d	STR-308	02-Feb-27	16-Feb-27	68.20d																																		
197		 MEP-040 Fire Fighting Risers	10.00d	STR-308	02-Feb-27	13-Feb-27	79.20d																																		
198		 MEP-050 HVAC Risers	10.00d	STR-308	02-Feb-27	13-Feb-27	76.20d																																		
199		 MEP-060 Main Electrical Panel Installation	5.00d	PROC-090, STR-608	18-Mar-27	24-Mar-27	37.40d																																		
200		 MEP-070 Distribution Boards Installation	8.00d	MEP-060	24-Mar-27	02-Apr-27	37.40d																																		
201		 MEP-080 Main Cable Pulling	8.00d	MEP-030, MEP-060	24-Mar-27	02-Apr-27	37.40d																																		
202		 MEP-090 Pumps Installation	5.00d	PROC-080, STR-608	18-Mar-27	24-Mar-27	46.40d																																		
203		 MEP-100 Water Tanks Installation	5.00d	STR-608	18-Mar-27	24-Mar-27	68.40d																																		
204	 MEP-110 Fire Alarm Main Panel	4.00d	PROC-110, STR-608	18-Mar-27	23-Mar-27	47.40d																																			
205	 MEP-120 HVAC Equipment Installation	8.00d	PROC-100, STR-608	18-Mar-27	27-Mar-27	40.40d																																			
206	SP1.8.5 Lift			77.60d		18-Jan-27	19-Apr-27	23.40d																																	
207		 LFT-010 Lift Shaft Readiness Inspection	2.00d	STR-608	18-Mar-27	20-Mar-27	23.40d																																		
208		 LFT-020 Lift Equipment Delivery	0.00d	PROC-120		18-Jan-27	76.00d																																		
209		 LFT-030 Lift Installation	20.00d	LFT-010, LFT-020	20-Mar-27	13-Apr-27	23.40d																																		
210	 LFT-040 Lift Testing & Certification	5.00d	LFT-030	13-Apr-27	19-Apr-27	23.40d																																			
211	SP1.9.0 External Works			35.00d		18-Mar-27	28-Apr-27	38.40d																																	
212		 EXT-010 External Drainage	8.00d	M-020	18-Mar-27	27-Mar-27	9.40d																																		
213		 EXT-020 External Water Network	6.00d	EXT-010	27-Mar-27	03-Apr-27	9.40d																																		
214		 EXT-030 External Electrical Services	6.00d	EXT-010	27-Mar-27	03-Apr-27	9.40d																																		
215		 EXT-040 Boundary Wall	10.00d	M-020	18-Mar-27	30-Mar-27	63.40d																																		
216		 EXT-050 Kerbs & Paving	10.00d	EXT-010, EXT-020, EXT-030	03-Apr-27	15-Apr-27	9.40d																																		
217		 EXT-060 Car Parking	8.00d	EXT-050	15-Apr-27	24-Apr-27	9.40d																																		
218		 EXT-070 Landscaping	8.00d	EXT-050	15-Apr-27	24-Apr-27	12.40d																																		
219		 EXT-080 External Lighting	5.00d	EXT-030, EXT-050	15-Apr-27	21-Apr-27	15.40d																																		
220		 EXT-090 Road Marking / Signage	3.00d	EXT-060	24-Apr-27	28-Apr-27	9.40d																																		
221	 EXT-100 External Works Complete	0.00d	EXT-070, EXT-080, EXT-090		28-Apr-27	9.40d																																			
222	SP1.10.0 Testing & Commissioning			36.40d		19-Apr-27	31-May-27	10.00d																																	
223		 T&C-010 Electrical Testing	5.00d	ARC-515, MEP-070, MEP-080	10-May-27	14-May-27	6.00d																																		
224		 T&C-020 Plumbing Pressure Testing	4.00d	ARC-515, MEP-020, MEP-090	10-May-27	13-May-27	7.00d																																		
225		 T&C-030 Drainage Testing	3.00d	ARC-515, MEP-010	10-May-27	12-May-27	8.00d																																		
226		 T&C-040 Fire Fighting Testing	4.00d	ARC-515, MEP-040	10-May-27	13-May-27	7.00d																																		
227		 T&C-050 Fire Alarm Testing	4.00d	ARC-515, MEP-110	10-May-27	13-May-27	7.00d																																		
228		 T&C-060 HVAC Testing & Balancing	7.00d	ARC-515, MEP-050, MEP-120	10-May-27	17-May-27	4.00d																																		
229	 T&C-070 Lift Final Testing	5.00d	LFT-040	19-Apr-27	24-Apr-27	23.40d																																			

