


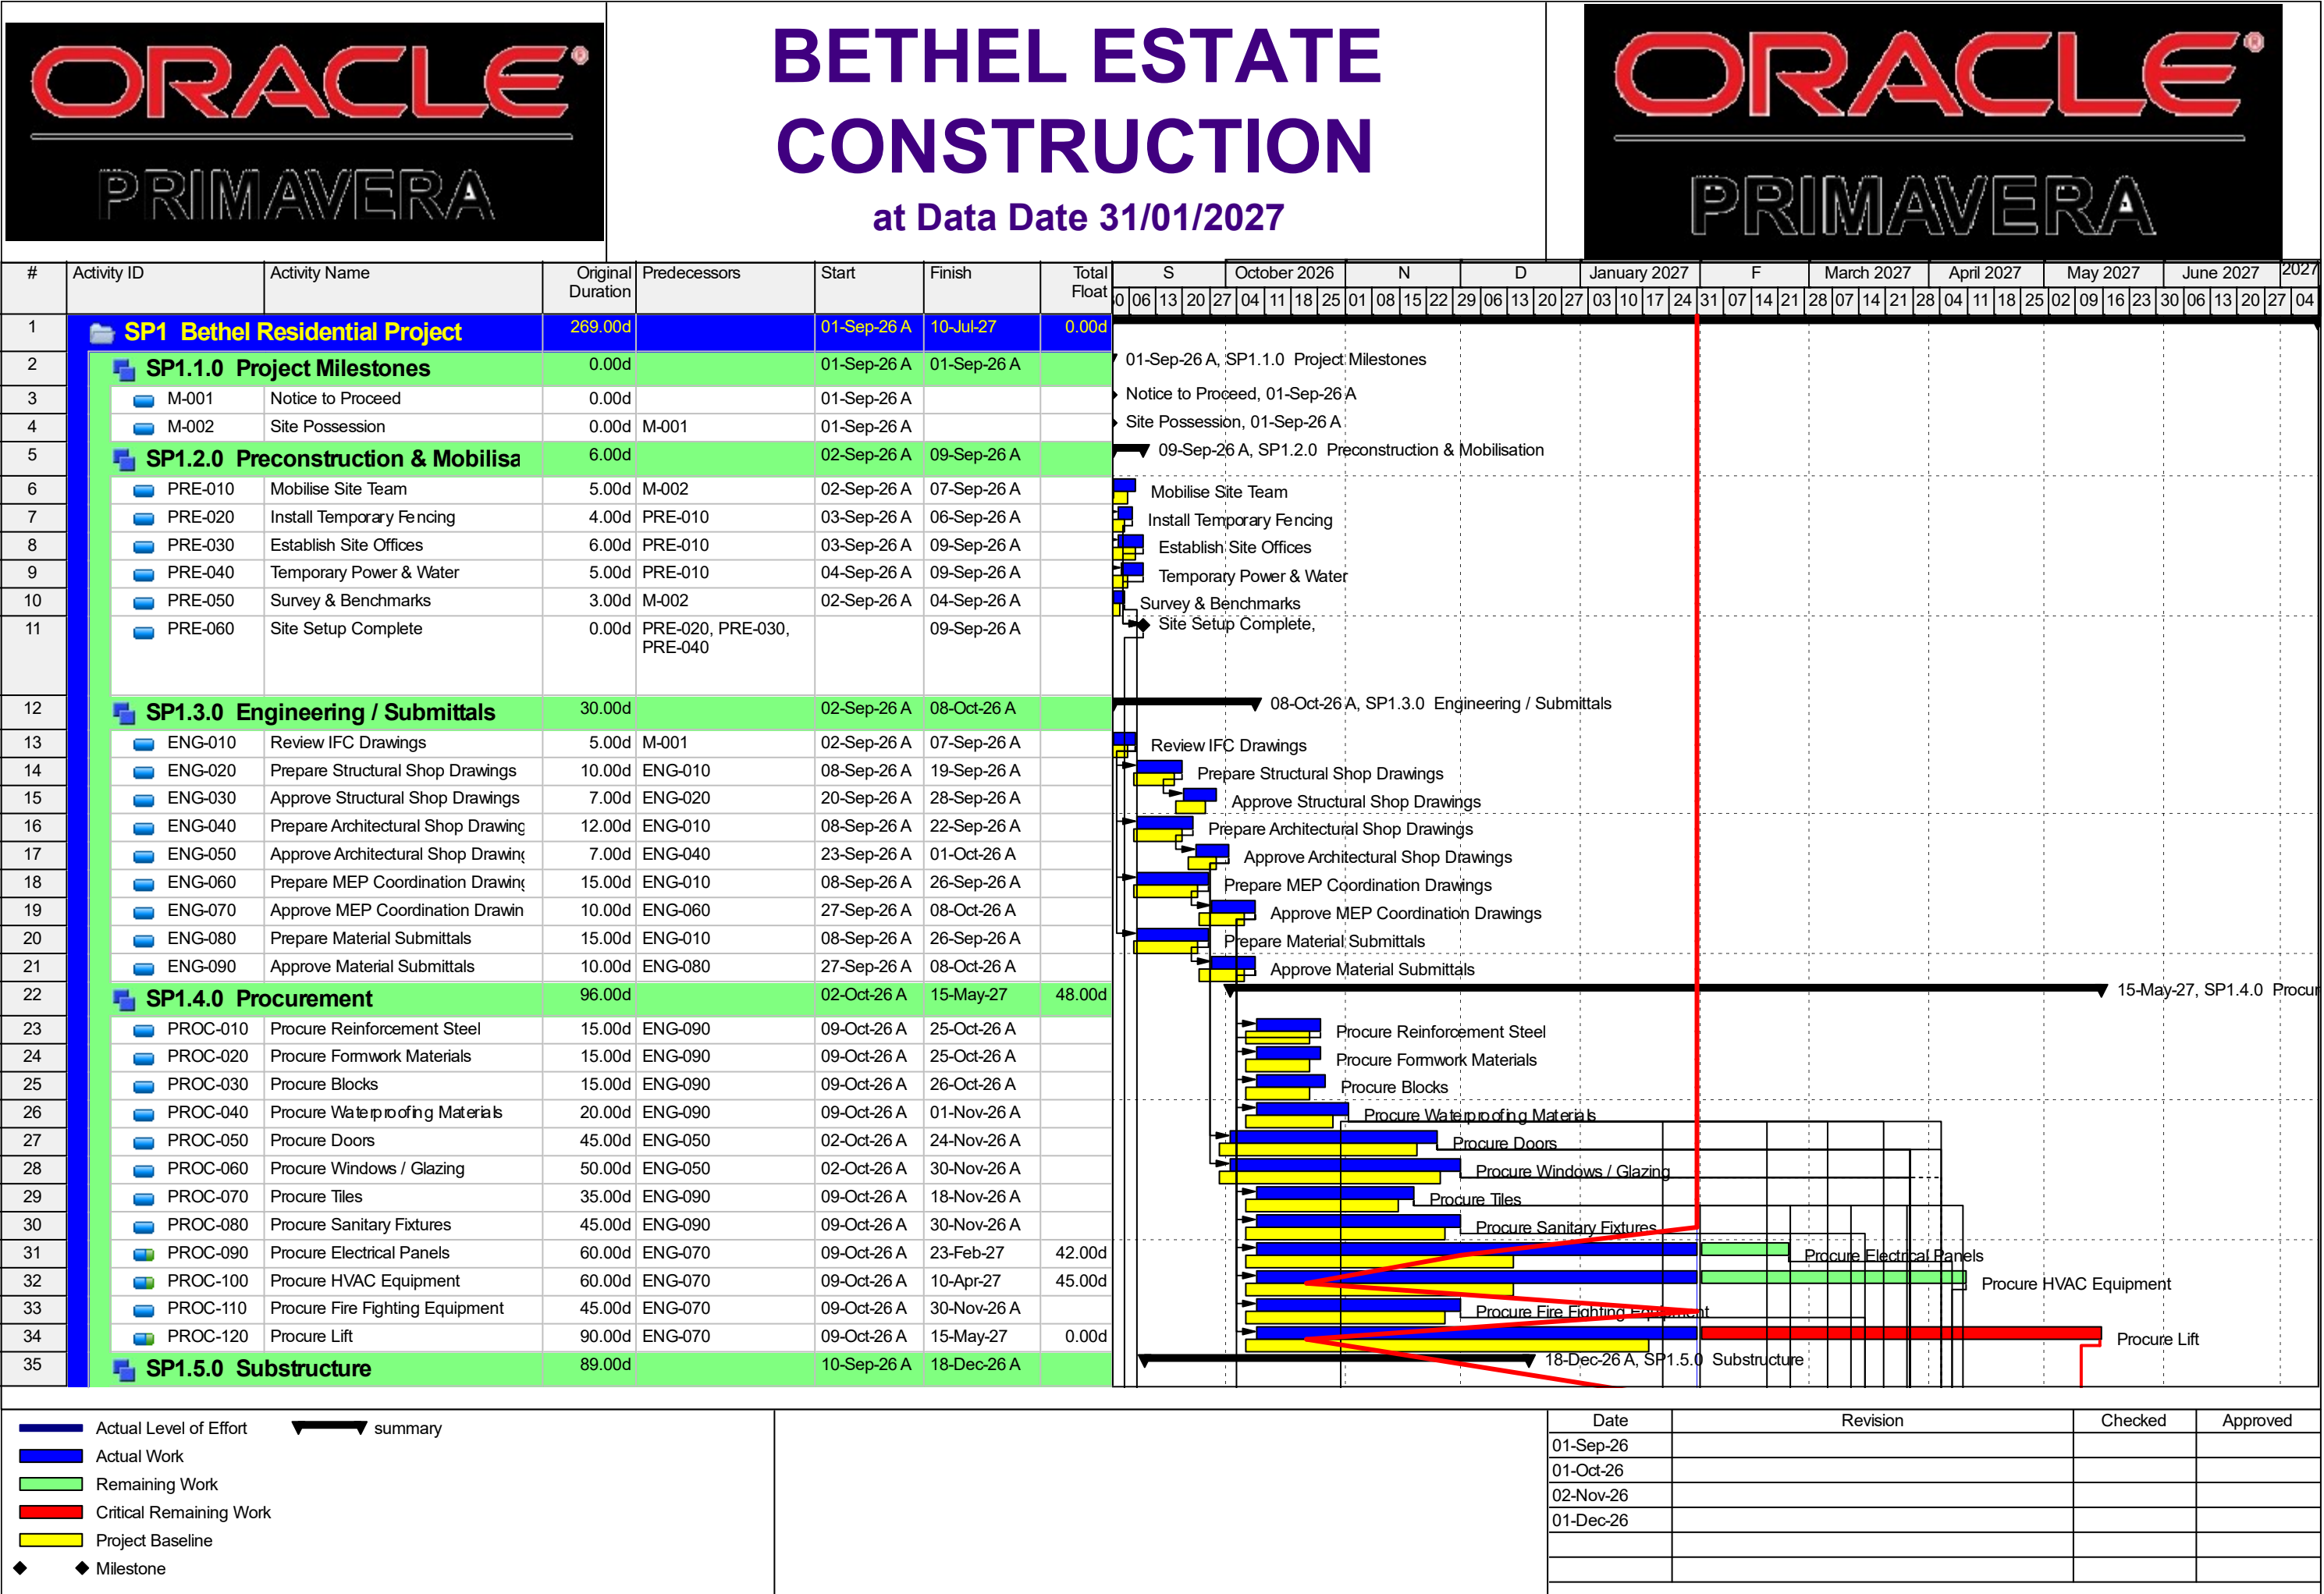

#	Activity ID	Activity Name	Original Duration	Predecessors	Start	Finish	Total Float
36	M-010	Substructure Complete	0.00d	SUB-190		05-Dec-26 A	
37	SUB-010	Site Clearing	3.00d	PRE-060	10-Sep-26 A	12-Sep-26 A	
38	SUB-020	Setting Out	2.00d	PRE-050, SUB-010	13-Sep-26 A	14-Sep-26 A	
39	SUB-030	Bulk Excavation	8.00d	SUB-020	15-Sep-26 A	24-Sep-26 A	
40	SUB-040	Excavation to Foundations	5.00d	SUB-030	25-Sep-26 A	30-Sep-26 A	
41	SUB-050	PCC / Blinding	3.00d	SUB-040	01-Oct-26 A	04-Oct-26 A	
42	SUB-060	Foundation Waterproofing Preparation	3.00d	SUB-050	05-Oct-26 A	07-Oct-26 A	
43	SUB-070	Footing Reinforcement	6.00d	SUB-050, PROC-010	09-Oct-26 A	15-Oct-26 A	
44	SUB-080	Footing Formwork	4.00d	SUB-070	11-Oct-26 A	15-Oct-26 A	
45	SUB-090	Footing Concrete	2.00d	SUB-070, SUB-080	16-Oct-26 A	17-Oct-26 A	
46	SUB-100	Foundation Columns Reinforcement	5.00d	SUB-090	18-Oct-26 A	23-Oct-26 A	
47	SUB-110	Foundation Columns Concrete	2.00d	SUB-100	24-Oct-26 A	25-Oct-26 A	
48	SUB-120	Grade / Ground Beams	8.00d	SUB-110	26-Oct-26 A	04-Nov-26 A	
49	SUB-130	Underground Drainage	6.00d	SUB-120	05-Nov-26 A	11-Nov-26 A	
50	SUB-140	Foundation Waterproofing	5.00d	SUB-120, PROC-040	05-Nov-26 A	10-Nov-26 A	
51	SUB-150	Backfilling & Compaction	6.00d	SUB-130, SUB-140	12-Nov-26 A	18-Dec-26 A	
52	SUB-160	Ground Floor Underground Service	5.00d	SUB-150	19-Nov-26 A	24-Nov-26 A	
53	SUB-170	Hardcore / Sub-base	4.00d	SUB-160	25-Nov-26 A	29-Nov-26 A	
54	SUB-180	DPM & Slab Reinforcement	4.00d	SUB-170	30-Nov-26 A	03-Dec-26 A	
55	SUB-190	Ground Floor Slab Concrete	2.00d	SUB-180	04-Dec-26 A	05-Dec-26 A	
56	SP1.6 Superstructure		77.80d		06-Dec-26 A	20-Mar-27	32.20d
57	M-020	Superstructure Complete	0.00d	STR-608		20-Mar-27	32.20d
58	SP1.6.1 Superstructure – First Floor		12.60d		06-Dec-26 A	18-Jan-27 A	
59	STR-101	1F Columns / Shear Walls Rebar	4.00d	M-010	06-Dec-26 A	09-Dec-26 A	
60	STR-102	1F Columns / Shear Walls Formwork	3.00d	STR-101	07-Dec-26 A	10-Dec-26 A	
61	STR-103	1F Columns / Shear Walls Concrete	1.00d	STR-101, STR-102	11-Dec-26 A	11-Dec-26 A	
62	STR-104	1F Slab / Beam Formwork	5.00d	STR-103	12-Dec-26 A	17-Dec-26 A	
63	STR-105	1F Slab / Beam Rebar	4.00d	STR-104	14-Dec-26 A	18-Jan-27 A	
64	STR-106	1F MEP Embedded Services	2.00d	STR-105	16-Dec-26 A	18-Dec-26 A	
65	STR-107	1F Slab Inspection	1.00d	STR-104, STR-105, STR-106	19-Dec-26 A	19-Dec-26 A	
66	STR-108	1F Slab Concrete	1.00d	STR-107	20-Dec-26 A	20-Dec-26 A	
67	SP1.6.2 Superstructure – Second Floor		23.80d		21-Dec-26 A	04-Jan-27 A	
68	STR-201	2F Columns / Shear Walls Rebar	4.00d	STR-108	21-Dec-26 A	24-Dec-26 A	
69	STR-202	2F Columns / Shear Walls Formwork	3.00d	STR-201	22-Dec-26 A	25-Dec-26 A	
70	STR-203	2F Columns / Shear Walls Concrete	1.00d	STR-201, STR-202	26-Dec-26 A	26-Dec-26 A	
71	STR-204	2F Slab / Beam Formwork	5.00d	STR-203	27-Dec-26 A	01-Jan-27 A	
72	STR-205	2F Slab / Beam Rebar	4.00d	STR-204	29-Dec-26 A	02-Jan-27 A	
73	STR-206	2F MEP Embedded Services	2.00d	STR-205	31-Dec-26 A	02-Jan-27 A	
74	STR-207	2F Slab Inspection	1.00d	STR-204, STR-205, STR-206	03-Jan-27 A	03-Jan-27 A	
75	STR-208	2F Slab Concrete	1.00d	STR-207	04-Jan-27 A	04-Jan-27 A	
76	SP1.6.3 Superstructure – Third Floor		14.80d		05-Jan-27 A	04-Feb-27	22.80d
77	STR-301	3F Columns / Shear Walls Rebar	4.00d	STR-208	05-Jan-27 A	09-Jan-27 A	
78	STR-302	3F Columns / Shear Walls Formwork	3.00d	STR-301	06-Jan-27 A	10-Jan-27 A	
79	STR-303	3F Columns / Shear Walls Concrete	1.00d	STR-301, STR-302	11-Jan-27 A	11-Jan-27 A	

[illegible]

#	Activity ID	Activity Name	Original Duration	Predecessors	Start	Finish	Total Float	2027																																												
								S	October 2026					N					D					January 2027				F				March 2027				April 2027				May 2027				June 2027				2027				
								0	06	13	20	27	04	11	18	25	01	08	15	22	29	06	13	20	27	03	10	17	24	31	07	14	21	28	07	14	21	28	04	11	18	25	02	09	16	23	30	06	13	20	27	04
121		 ARC-108	1F Doors & Windows	5.00d	ARC-103, PROC-050, PROC-060	01-Apr-27	06-Apr-27	67.00d																																												
122		 ARC-109	1F False Ceiling	5.00d	ARC-106	06-Feb-27	11-Feb-27	112.00d																																												
123		 ARC-110	1F First Coat Painting	5.00d	ARC-103	01-Feb-27	05-Feb-27	117.00d																																												
124		 ARC-111	1F MEP Second Fix	6.00d	ARC-107, ARC-109, ARC-110	15-Feb-27	20-Feb-27	110.00d																																												
125		 ARC-112	1F Joinery & Fixtures	5.00d	ARC-107, ARC-108	07-Apr-27	12-Apr-27	67.00d																																												
126		 ARC-113	1F Final Painting	4.00d	ARC-111, ARC-112	13-Apr-27	16-Apr-27	67.00d																																												
127		 ARC-114	1F Final Floor Finishes	4.00d	ARC-113	17-Apr-27	21-Apr-27	67.00d																																												
128		 ARC-115	1F Final Cleaning	2.00d	ARC-114	22-Apr-27	23-Apr-27	67.00d																																												
129		 SP1.7.2 Architectural – Second Floor	69.20d		20-Jan-27 A	23-Apr-27	67.00d																																													
130		 ARC-201	2F Blockwork	8.00d	STR-308	20-Jan-27 A	13-Feb-27	91.00d																																												
131		 ARC-202	2F MEP First Fix	7.00d	ARC-201	24-Jan-27 A	12-Feb-27	92.00d																																												
132		 ARC-203	2F Internal Plaster	7.00d	ARC-201, ARC-202	15-Feb-27	22-Feb-27	91.00d																																												
133		 ARC-204	2F Wet Area Waterproofing	4.00d	ARC-203, PROC-040	23-Feb-27	26-Feb-27	92.00d																																												
134		 ARC-205	2F Floor Screed	5.00d	ARC-203	22-Feb-27 A	27-Feb-27	91.00d																																												
135		 ARC-206	2F Ceiling Framing	5.00d	ARC-203	23-Feb-27	27-Feb-27	93.00d																																												
136		 ARC-207	2F Wall / Floor Tiling	7.00d	ARC-204, ARC-205, PROC-070	01-Mar-27	08-Mar-27	91.00d																																												
137		 ARC-208	2F Doors & Windows	5.00d	ARC-203, PROC-050, PROC-060	01-Apr-27	06-Apr-27	67.00d																																												
138		 ARC-209	2F False Ceiling	5.00d	ARC-206	01-Mar-27	05-Mar-27	93.00d																																												
139		 ARC-210	2F First Coat Painting	5.00d	ARC-203	23-Feb-27	27-Feb-27	98.00d																																												
140		 ARC-211	2F MEP Second Fix	6.00d	ARC-207, ARC-209, ARC-210	09-Mar-27	15-Mar-27	91.00d																																												
141		 ARC-212	2F Joinery & Fixtures	5.00d	ARC-207, ARC-208	07-Apr-27	12-Apr-27	67.00d																																												
142		 ARC-213	2F Final Painting	4.00d	ARC-211, ARC-212	13-Apr-27	16-Apr-27	67.00d																																												
143		 ARC-214	2F Final Floor Finishes	4.00d	ARC-213	17-Apr-27	21-Apr-27	67.00d																																												
144		 ARC-215	2F Final Cleaning	2.00d	ARC-214	22-Apr-27	23-Apr-27	67.00d																																												
145		 SP1.7.3 Architectural – Third Floor	54.40d		19-Feb-27 A	23-Apr-27	67.00d																																													
146		 ARC-301	3F Blockwork	8.00d	STR-408	19-Feb-27	01-Mar-27	77.00d																																												
147		 ARC-302	3F MEP First Fix	7.00d	ARC-301	23-Feb-27	02-Mar-27	77.00d																																												
148		 ARC-303	3F Internal Plaster	7.00d	ARC-301, ARC-302	03-Mar-27	10-Mar-27	77.00d																																												
149		 ARC-304	3F Wet Area Waterproofing	4.00d	ARC-303, PROC-040	11-Mar-27	15-Mar-27	78.00d																																												
150		 ARC-305	3F Floor Screed	5.00d	ARC-303	11-Mar-27	16-Mar-27	77.00d																																												
151		 ARC-306	3F Ceiling Framing	5.00d	ARC-303	11-Mar-27	16-Mar-27	79.00d																																												
152		 ARC-307	3F Wall / Floor Tiling	7.00d	ARC-304, ARC-305, PROC-070	17-Mar-27	24-Mar-27	77.00d																																												
153		 ARC-308	3F Doors & Windows	5.00d	ARC-303, PROC-050, PROC-060	01-Apr-27	06-Apr-27	67.00d																																												
154		 ARC-309	3F False Ceiling	5.00d	ARC-306	17-Mar-27	22-Mar-27	79.00d																																												
155		 ARC-310	3F First Coat Painting	5.00d	ARC-303	11-Mar-27	16-Mar-27	84.00d																																												

#	Activity ID	Activity Name	Original Duration	Predecessors	Start	Finish	Total Float	S							October 2026							N							D							January 2027							F							March 2027							April 2027							May 2027							June 2027							2027
								0	06	13	20	27	04	11	18	25	01	08	15	22	29	06	13	20	27	03	10	17	24	31	07	14	21	28	04	11	18	25	02	09	16	23	30	06	13	20	27	04																														
156		ARC-311	3F MEP Second Fix	6.00d	ARC-307, ARC-309, ARC-310	25-Mar-27	31-Mar-27	77.00d																																																																						
157		ARC-312	3F Joinery & Fixtures	5.00d	ARC-307, ARC-308	07-Apr-27	12-Apr-27	67.00d																																																																						
158		ARC-313	3F Final Painting	4.00d	ARC-311, ARC-312	29-Mar-27 A	16-Apr-27	67.00d																																																																						
159		ARC-314	3F Final Floor Finishes	4.00d	ARC-313	17-Apr-27	21-Apr-27	67.00d																																																																						
160		ARC-315	3F Final Cleaning	2.00d	ARC-314	22-Apr-27	23-Apr-27	67.00d																																																																						
161		SP1.7.4 Architectural – Fourth Floor	44.40d		06-Mar-27	27-Apr-27	64.40d																																																																							
162		ARC-401	4F Blockwork	8.00d	STR-508	06-Mar-27	16-Mar-27	64.40d																																																																						
163		ARC-402	4F MEP First Fix	7.00d	ARC-401	09-Mar-27	17-Mar-27	64.40d																																																																						
164		ARC-403	4F Internal Plaster	7.00d	ARC-401, ARC-402	17-Mar-27	25-Mar-27	64.40d																																																																						
165		ARC-404	4F Wet Area Waterproofing	4.00d	ARC-403, PROC-040	25-Mar-27	30-Mar-27	65.40d																																																																						
166		ARC-405	4F Floor Screed	5.00d	ARC-403	25-Mar-27	31-Mar-27	64.40d																																																																						
167		ARC-406	4F Ceiling Framing	5.00d	ARC-403	25-Mar-27	31-Mar-27	66.40d																																																																						
168		ARC-407	4F Wall / Floor Tiling	7.00d	ARC-404, ARC-405, PROC-070	31-Mar-27	08-Apr-27	64.40d																																																																						
169		ARC-408	4F Doors & Windows	5.00d	ARC-403, PROC-050, PROC-060	01-Apr-27	06-Apr-27	67.00d																																																																						
170		ARC-409	4F False Ceiling	5.00d	ARC-406	31-Mar-27	06-Apr-27	66.40d																																																																						
171		ARC-410	4F First Coat Painting	5.00d	ARC-403	25-Mar-27	31-Mar-27	71.40d																																																																						
172		ARC-411	4F MEP Second Fix	6.00d	ARC-407, ARC-409, ARC-410	08-Apr-27	15-Apr-27	64.40d																																																																						
173		ARC-412	4F Joinery & Fixtures	5.00d	ARC-407, ARC-408	08-Apr-27	14-Apr-27	65.40d																																																																						
174		ARC-413	4F Final Painting	4.00d	ARC-411, ARC-412	15-Apr-27	20-Apr-27	64.40d																																																																						
175		ARC-414	4F Final Floor Finishes	4.00d	ARC-413	20-Apr-27	24-Apr-27	64.40d																																																																						
176		ARC-415	4F Final Cleaning	2.00d	ARC-414	24-Apr-27	27-Apr-27	64.40d																																																																						
177		SP1.7.5 Architectural – Fifth Floor	44.40d		20-Mar-27 A	12-May-27	22.80d																																																																							
178		ARC-501	5F Blockwork	8.00d	STR-608	20-Mar-27	30-Mar-27	22.80d																																																																						
179		ARC-502	5F MEP First Fix	7.00d	ARC-501	24-Mar-27	01-Apr-27	22.80d																																																																						
180		ARC-503	5F Internal Plaster	7.00d	ARC-501, ARC-502	01-Apr-27	09-Apr-27	22.80d																																																																						
181		ARC-504	5F Wet Area Waterproofing	4.00d	ARC-503, PROC-040	09-Apr-27	14-Apr-27	23.80d																																																																						
182		ARC-505	5F Floor Screed	5.00d	ARC-503	09-Apr-27	15-Apr-27	22.80d																																																																						
183		ARC-506	5F Ceiling Framing	5.00d	ARC-503	07-Apr-27 A	15-Apr-27	24.80d																																																																						
184		ARC-507	5F Wall / Floor Tiling	7.00d	ARC-504, ARC-505, PROC-070	15-Apr-27	23-Apr-27	22.80d																																																																						
185		ARC-508	5F Doors & Windows	5.00d	ARC-503, PROC-050, PROC-060	09-Apr-27	15-Apr-27	30.80d																																																																						
186		ARC-509	5F False Ceiling	5.00d	ARC-506	15-Apr-27	21-Apr-27	24.80d																																																																						
187		ARC-510	5F First Coat Painting	5.00d	ARC-503	09-Apr-27	15-Apr-27	29.80d																																																																						
188		ARC-511	5F MEP Second Fix	6.00d	ARC-507, ARC-509, ARC-510	23-Apr-27	30-Apr-27	22.80d																																																																						
189		ARC-512	5F Joinery & Fixtures	5.00d	ARC-507, ARC-508	23-Apr-27	29-Apr-27	23.80d																																																																						
190	ARC-513	5F Final Painting	4.00d	ARC-511, ARC-512	30-Apr-27	05-May-27	22.80d																																																																							
191	ARC-514	5F Final Floor Finishes	4.00d	ARC-513	05-May-27	10-May-27	22.80d																																																																							

