




#	Activity ID	Activity Name	Original Duration	Predecessors	Start	Finish	Total Float	2027																																																								
								S	October 2026					November 2026					December 2026					January 2027					February 2027					March 2027					April 2027					May 2027																				
								0	06	13	20	27		04	11	18	25		01	08	15	22		29	06	13	20	27	03	10	17	24	31	07	14	21	28	07	14	21	28	04	11	18	25	02	09	16	23	30	06													
33		 STR-201	2F Columns / Shear Walls Rebar	4.00d	STR-108	04-Jan-27 A	08-Jan-27	0.00d																										2F Columns / Shear Walls Rebar																														
34		 STR-203	2F Columns / Shear Walls Concrete	1.00d	STR-201, STR-202	08-Jan-27	09-Jan-27	0.00d																										2F Columns / Shear Walls Concrete																														
35		 STR-204	2F Slab / Beam Formwork	5.00d	STR-203	09-Jan-27	15-Jan-27	0.00d																										2F Slab / Beam Formwork																														
36		 STR-205	2F Slab / Beam Rebar	4.00d	STR-204	12-Jan-27	16-Jan-27	0.00d																										2F Slab / Beam Rebar																														
37		 STR-207	2F Slab Inspection	1.00d	STR-204, STR-205, STR-206	16-Jan-27	18-Jan-27	0.00d																										2F Slab Inspection																														
38		 STR-208	2F Slab Concrete	1.00d	STR-207	18-Jan-27	19-Jan-27	0.00d																										2F Slab Concrete																														
39		 SP1.6.3 Superstructure – Third Floor		12.60d		19-Jan-27	02-Feb-27	0.00d																									 02-Feb-27, SP1.6.3 Superstructure – Third Floor																															
40		 STR-301	3F Columns / Shear Walls Rebar	4.00d	STR-208	19-Jan-27	23-Jan-27	0.00d																										3F Columns / Shear Walls Rebar																														
41		 STR-303	3F Columns / Shear Walls Concrete	1.00d	STR-301, STR-302	23-Jan-27	25-Jan-27	0.00d																										3F Columns / Shear Walls Concrete																														
42		 STR-304	3F Slab / Beam Formwork	5.00d	STR-303	25-Jan-27	30-Jan-27	0.00d																										3F Slab / Beam Formwork																														
43	 STR-305	3F Slab / Beam Rebar	4.00d	STR-304	26-Jan-27	30-Jan-27	0.00d																										3F Slab / Beam Rebar																															
44	 STR-307	3F Slab Inspection	1.00d	STR-304, STR-305, STR-306	30-Jan-27	01-Feb-27	0.00d																										3F Slab Inspection																															
45	 STR-308	3F Slab Concrete	1.00d	STR-307	01-Feb-27	02-Feb-27	0.00d																										3F Slab Concrete																															
46	 SP1.6.4 Superstructure – Fourth Floor		12.60d		02-Feb-27	17-Feb-27	0.00d																									 17-Feb-27, SP1.6.4 Superstructure – Fourth Floor																																
47	 STR-401	4F Columns / Shear Walls Rebar	4.00d	STR-308	02-Feb-27	06-Feb-27	0.00d																										4F Columns / Shear Walls Rebar																															
48	 STR-403	4F Columns / Shear Walls Concrete	1.00d	STR-401, STR-402	06-Feb-27	08-Feb-27	0.00d																										4F Columns / Shear Walls Concrete																															
49	 STR-404	4F Slab / Beam Formwork	5.00d	STR-403	08-Feb-27	13-Feb-27	0.00d																										4F Slab / Beam Formwork																															
50	 STR-405	4F Slab / Beam Rebar	4.00d	STR-404	10-Feb-27	15-Feb-27	0.00d																										4F Slab / Beam Rebar																															
51	 STR-407	4F Slab Inspection	1.00d	STR-404, STR-405, STR-406	15-Feb-27	16-Feb-27	0.00d																										4F Slab Inspection																															
52	 STR-408	4F Slab Concrete	1.00d	STR-407	16-Feb-27	17-Feb-27	0.00d																										4F Slab Concrete																															
53	 SP1.6.5 Superstructure – Fifth Floor		12.60d		17-Feb-27	03-Mar-27	0.00d																									 03-Mar-27, SP1.6.5 Superstructure – Fifth Floor																																
54	 STR-501	5F Columns / Shear Walls Rebar	4.00d	STR-408	17-Feb-27	22-Feb-27	0.00d																										5F Columns / Shear Walls Rebar																															
55	 STR-503	5F Columns / Shear Walls Concrete	1.00d	STR-501, STR-502	22-Feb-27	23-Feb-27	0.00d																										5F Columns / Shear Walls Concrete																															
56	 STR-504	5F Slab / Beam Formwork	5.00d	STR-503	23-Feb-27	01-Mar-27	0.00d																										5F Slab / Beam Formwork																															
57	 STR-505	5F Slab / Beam Rebar	4.00d	STR-504	25-Feb-27	01-Mar-27	0.00d																										5F Slab / Beam Rebar																															
58	 STR-507	5F Slab Inspection	1.00d	STR-504, STR-505, STR-506	02-Mar-27	02-Mar-27	0.00d																										5F Slab Inspection																															
59	 STR-508	5F Slab Concrete	1.00d	STR-507	03-Mar-27	03-Mar-27	0.00d																										5F Slab Concrete																															
60	 SP1.6.6 Superstructure – Roof		12.60d		04-Mar-27	18-Mar-27	0.00d																									 18-Mar-27, SP1.6.6 Superstructure – Roof																																
61	 STR-601	RF Columns / Shear Walls Rebar	4.00d	STR-508	04-Mar-27	08-Mar-27	0.00d																										RF Columns / Shear Walls Rebar																															
62	 STR-603	RF Columns / Shear Walls Concrete	1.00d	STR-601, STR-602	09-Mar-27	09-Mar-27	0.00d																										RF Columns / Shear Walls Concrete																															
63	 STR-604	RF Slab / Beam Formwork	5.00d	STR-603	10-Mar-27	15-Mar-27	0.00d																										RF Slab / Beam Formwork																															
64	 STR-605	RF Slab / Beam Rebar	4.00d	STR-604	11-Mar-27	16-Mar-27	0.00d																										RF Slab / Beam Rebar																															
65	 STR-607	RF Slab Inspection	1.00d	STR-604, STR-605, STR-606	16-Mar-27	17-Mar-27	0.00d																										RF Slab Inspection																															
66	 STR-608	RF Slab Concrete	1.00d	STR-607	17-Mar-27	18-Mar-27	0.00d																										RF Slab Concrete																															
67	 SP1.7 Architectural		44.40d		18-Mar-27	08-May-27	0.00d																									 08-May-27, SP1.7																																
68	 SP1.7.1 Architectural – First Floor		0.00d				0.00d																																																									
69	 SP1.7.2 Architectural – Second Floor		0.00d				0.00d																																																									
70	 SP1.7.3 Architectural – Third Floor		0.00d				0.00d																																																									
71	 SP1.7.4 Architectural – Fourth Floor		0.00d				0.00d																																																									
72	 SP1.7.5 Architectural – Fifth Floor		44.40d		18-Mar-27	08-May-27	0.00d																									 08-May-27, SP1.7																																
73	 ARC-501	5F Blockwork	8.00d	STR-608	18-Mar-27	27-Mar-27	0.00d																										5F Blockwork																															
74	 ARC-502	5F MEP First Fix	7.00d	ARC-501	22-Mar-27	29-Mar-27	0.00d																										5F MEP First Fix																															

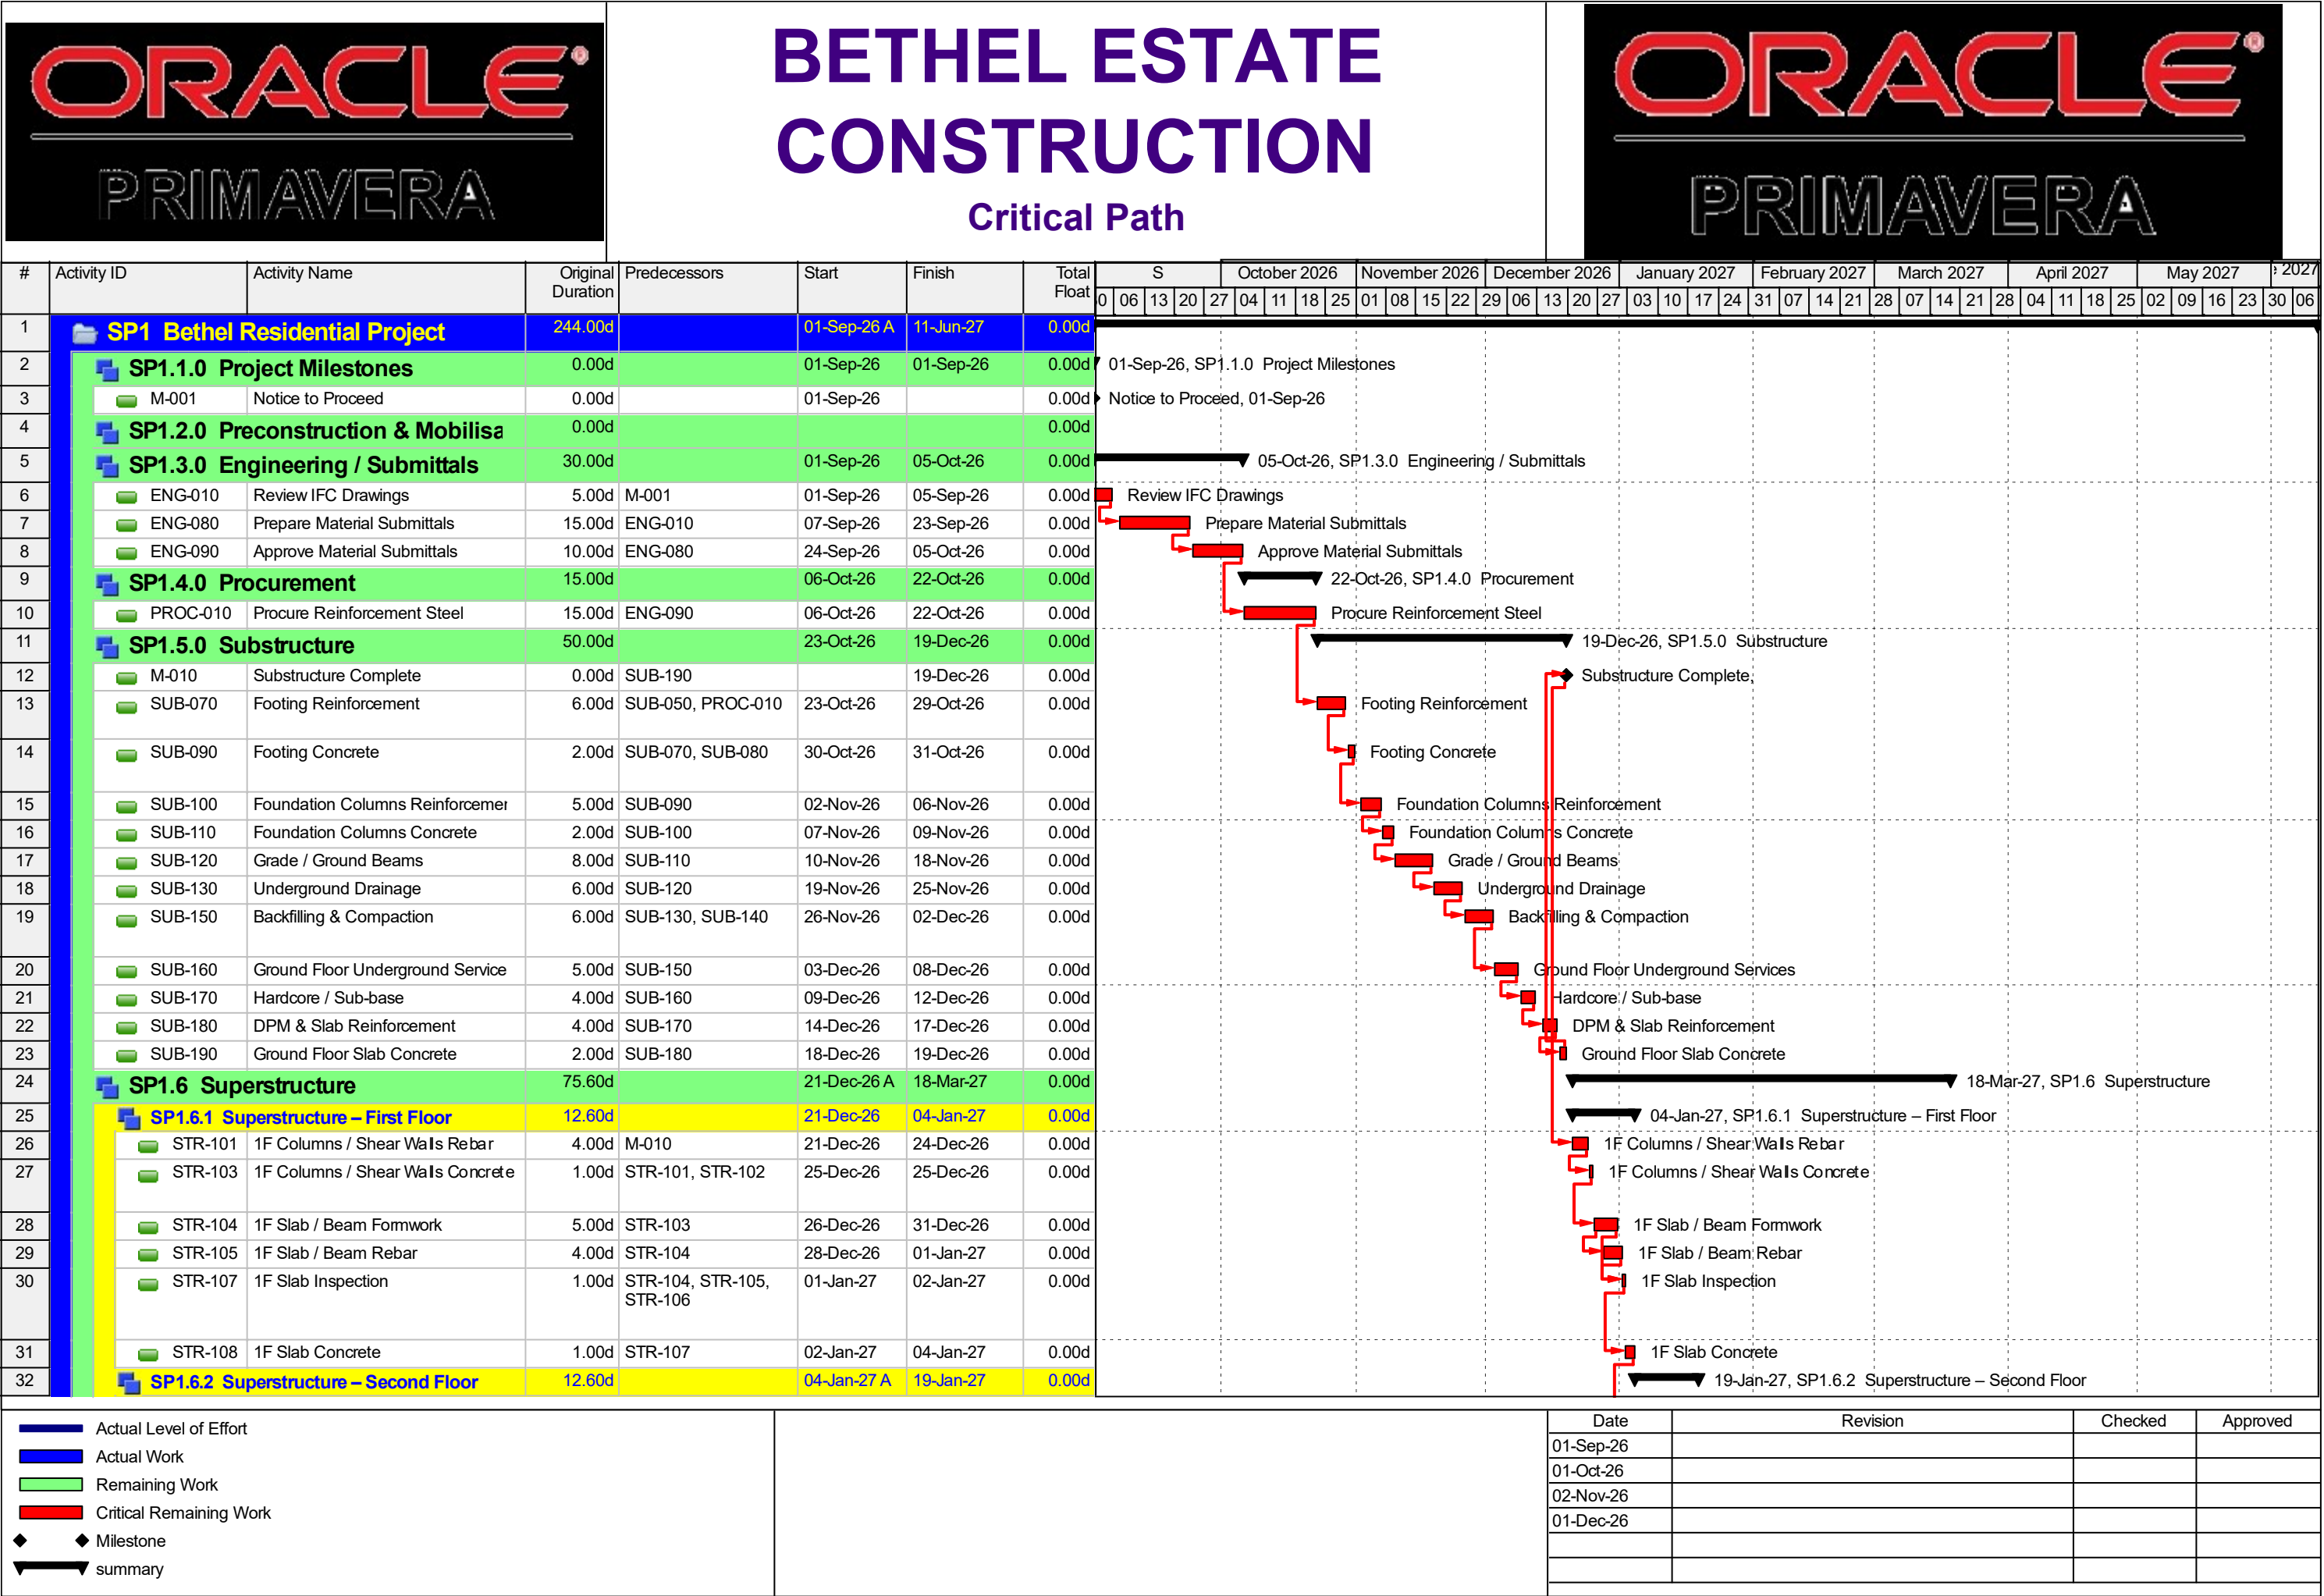
